

Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Problem Statement 60 — Podcast Guest Scheduling & Outline Builder
SHIKSHITH V

PES1UG24AM400

Section 5-G

1. Epics

- Epic 1 — Interview Scheduling: covers guest slot booking, host slot management, and calendar invites.
- Epic 2 — Guest Topic & Outline Management: covers guest topic outline submission, host review, and revision requests.
- Epic 3 — Episode Production: covers compiling approved outlines into the run-of-show production sheet.


2. Backlog — User Stories, Priority & Story Points

ID	Story	Epic	Priority	Points
PGSOB-5	Book Interview Slot	Interview Scheduling	High	5
PGSOB-4	Manage Available Interview Slots	Interview Scheduling	High	5
PGSOB-6	Receive Calendar Invite	Interview Scheduling	High	3
PGSOB-7	Submit Topic Outline	Guest Topic & Outline Management	High	5
PGSOB-8	Review Guest Outline	Guest Topic & Outline Management	Medium	3
PGSOB-9	Request Outline Revision	Guest Topic & Outline Management	Medium	3
PGSOB-10	Generate Production Sheet	Episode Production	High	8

Total backlog estimate: 32 story points across 7 user stories, split into two sprints (Sprint 1: 18 points / 4 stories; Sprint 2: 14 points / 3 stories).


3. Screenshots

3.1 Product Backlog (Epics + User Stories + Story Points)

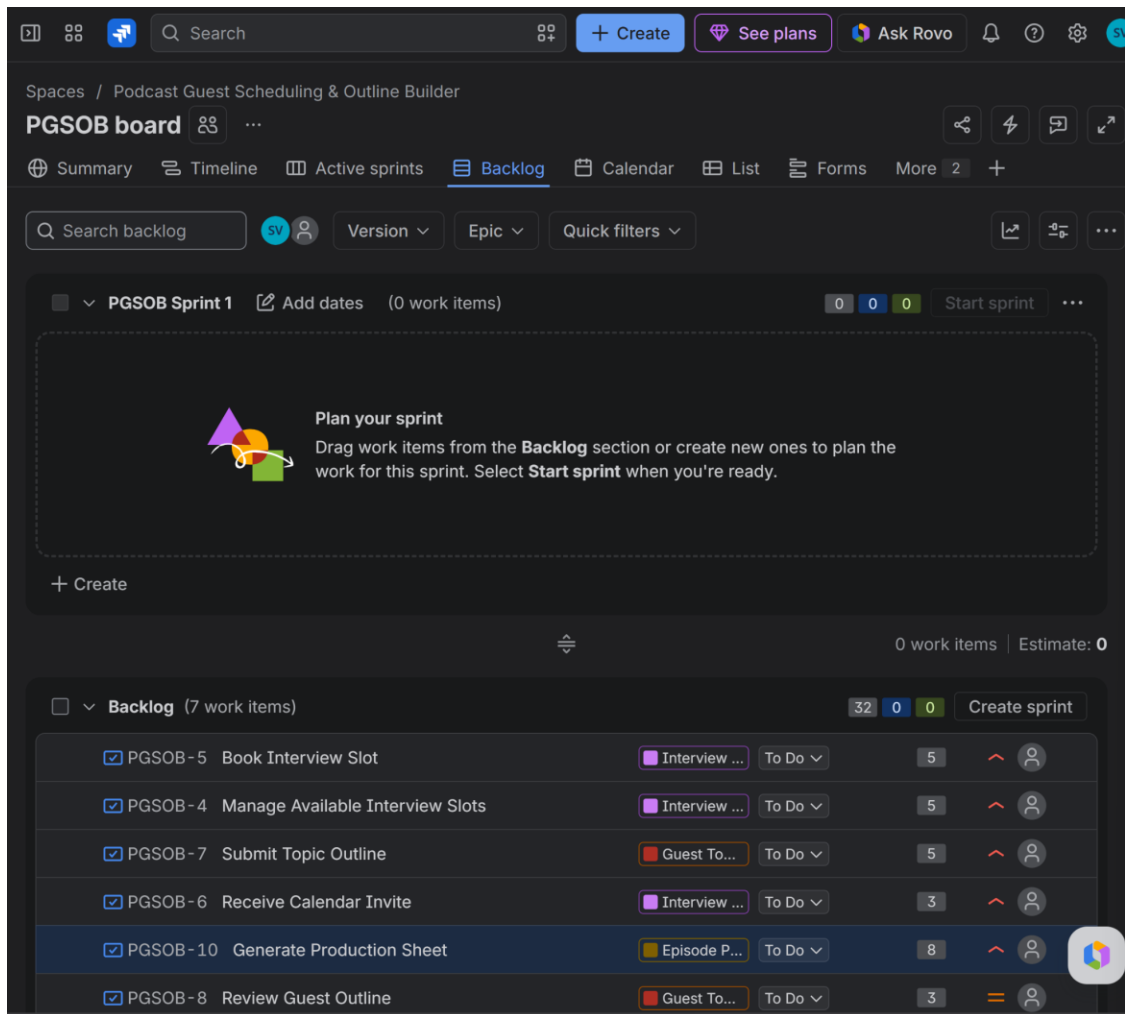


Jira Backlog view showing all user stories grouped under their epics, with story points assigned.

3.2 Sprint 1 — Completed Board

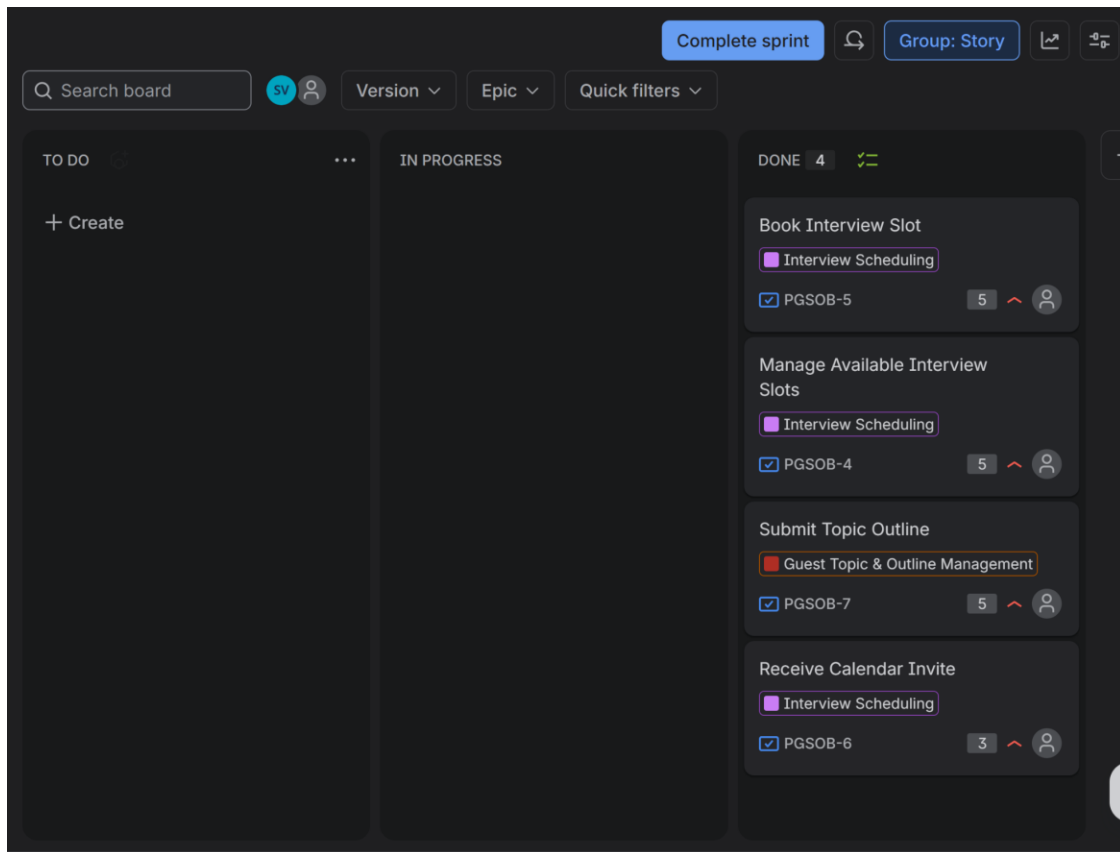


Sprint 1 (Interview Scheduling stories) — all 4 stories moved to Done, 18 points completed.

3.3 Sprint 2 — Completed Board

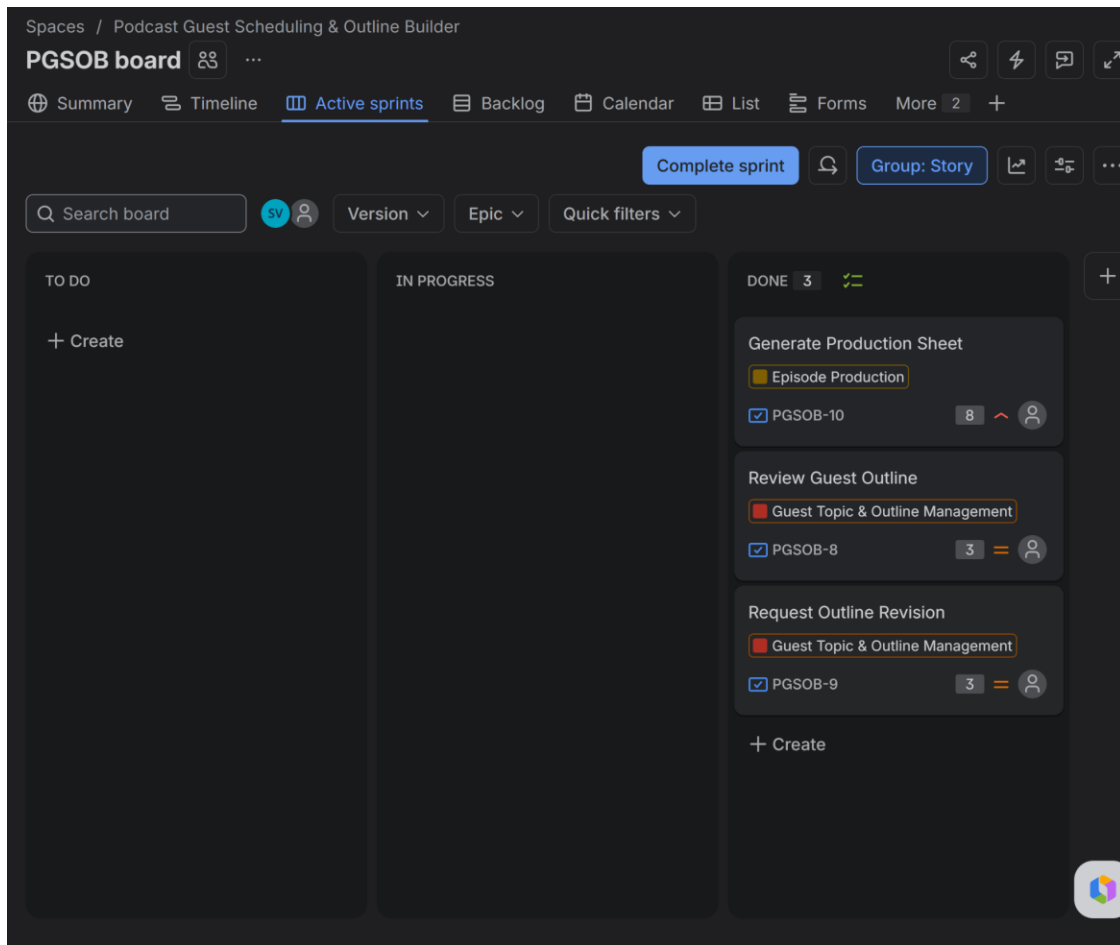

Sprint 2 (Guest Outline & Production stories) — all 3 stories moved to Done, 14 points completed.

3.4 Burndown Chart — Sprint 2

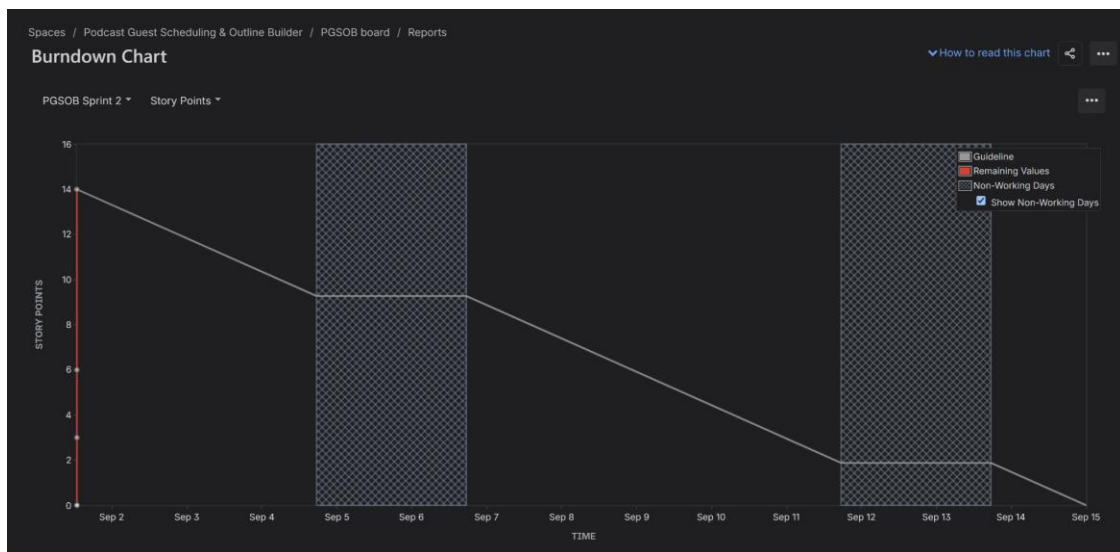

Sprint 2 burndown: remaining story points (red) dropped from 14 to 0 almost immediately, well ahead of the linear guideline (grey).

3.5 Burndown Event Log — Sprint 2

Date	Issue	Event Type	Event Detail	Story Points		
				Inc.	Dec.	Remaining
01/Sep/26 12:43 PM	PGSOB-10	Sprint start		8		
	PGSOB-8			3		
	PGSOB-9			3		
	Total					14
01/Sep/26 12:44 PM	PGSOB-10	Burndown	Issue completed	8	6	
	PGSOB-8	Burndown	Issue completed	3	3	
	PGSOB-9	Burndown	Issue completed	3	0	
01/Sep/26 12:46 PM	PGSOB-10	Sprint ended by SHIKSHITH V				0
	PGSOB-8					0
	PGSOB-9					0
	Total					0

Underlying burndown event log showing each issue's completion timestamp during Sprint 2.

4. Reflection Questions

1. Did your estimations reflect the actual effort?

Not directly — since this was a simulated sprint rather than real development work, all issues were marked Done within minutes of starting each sprint (see the Sprint 2 event log, where all 14 points were burned down between 12:43 PM and 12:46 PM). The story points themselves were still a reasonable relative measure of complexity: Generate Production Sheet was rightly the highest at 8 points, since it depends on compiling multiple guest outlines and generating a formatted PDF under a strict 1-second performance requirement (NFR-001), while smaller, more contained stories like Receive Calendar Invite were estimated lower at 3 points.

2. Was your backlog well-prioritized?

Yes. The core booking and outline-submission flows (Book Interview Slot, Manage Available Interview Slots, Receive Calendar Invite, Submit Topic Outline, Generate Production Sheet) were all marked High priority and scheduled across both sprints, since the system has no value without them. Review Guest Outline and Request Outline Revision were marked Medium, reflecting that they are secondary, optional flows (per FR-004) that support content quality but don't block the core booking-to-production pipeline.

3. How did your simulated sprint align with your plan?

Both sprints matched the intended split: Sprint 1 carried the Interview Scheduling epic end-to-end (booking, availability, invites) at 18 points, and Sprint 2 carried the Guest Topic & Outline Management and Episode Production epics at 14 points. Splitting by epic kept each sprint focused on delivering one complete slice of user-facing value rather than mixing unrelated features, which made it easy to track completion (all Sprint 1 and Sprint 2 stories reached Done).

4. What insights did the burndown chart give about your team's capacity?

The Sprint 2 burndown chart shows the remaining-points line (red) dropping from 14 to 0 almost vertically at the very start of the sprint window, while the guideline (grey) assumes a gradual, linear decline all the way to Sep 15. In a real project this shape would be a red flag: it suggests either the sprint length was set far longer than the actual work required, or the team drastically overestimated how long the work would take. For this lab, the near-instant burndown is expected since the tasks were simulated rather than actually built over the sprint duration — but the exercise still illustrates why the burndown chart is useful: a gap this large between the guideline and the actual line is exactly the kind of signal that would prompt a team to shorten future sprints or take on more work per sprint.
